


Sample Action Plan in Excel With Gantt Chart

Work Breakdown Structure (WBS)	WF %	Total Estimate	UM	Manpower			Equipment						Plan %	Plan QTY	Actual	Progress %
				Bar Bender	Form Worker	Worker	Truck Mixer	Concrete Pump	Crane	Excavator	Backhoe	Truck				
Civil Sample Project	100.00%															23.57%
Civil Work	97.13%	5,661.55														22.46%
Foundation	34.26%	2,378.43														56.29%
Pipe Rack	7.66%	182.19														74.01%
PR-45-001	100.00%	182.19														74.01%
Foundation Coating	2.00%	125.93	m2			4							100%	125.93		
Column Form Work	4.00%	322.92	m2		4				1				100%	322.92	154.88	47.96%
Column Concrete & Curing & Form	12.00%	60.55	m3			4	2	1					100%	60.55	45.17	74.59%
Foundation Back fill	4.00%	800.52	m3			4					1	2	100%	800.52		
Beam Reinforcement & Insert plate installation	3.00%	4,584.04	kg	5						1			100%	4,584.04	70.00	1.53%
Beam Form Work	3.00%	129.85	m2		5					1			100%	129.85	4.00	3.08%
Beam Concrete & Curing & Form work removing	9.00%	18.95	m3			4	2	1					100%	18.95		
Equipment RC Structure	92.34%	2,196.24											50%			54.81%
ST-20-005	2.13%	46.75											93%			7.00%
Lean Concrete	1.50%	4.96	m3			4	2	1					100%	4.96		
Rebar Supply	10.00%	4,533.40	kg										100%	4,533.40		
Reinforcement	32.00%	4,533.40	kg	3						1			100%	4,533.40		
Form Working	16.00%	14.00	m2		2					1			100%	14.00		
Bolt / Plat / Box Installation	2.00%	1,008.00	kg	3									100%	1,008.00		
Concrete Pouring	23.00%	46.75	m3			2	2	1					100%	46.75		
Curing & Form work removing	1.00%	100.00	%			2							100%	100.00		
Insulation	1.50%	14.00	m2		1								100%	14.00		
Back Filling	6.00%	228.65	m3			2					1	3	100%	228.65		
ST-30-001	74.83%	1,643.48											47%			57.09%
Foundation Coating	2.27%	470.52	m2			4							100%	470.52		
Foundation Back fill	4.55%	14,095.00	kg			4					1	3	100%	14,095.00		
Column Reinforcement & Insert plate & Anchore bolt installation	4.55%	169,622.86	kg	12						1			100%	169,622.86	137,228.29	80.90%
Column Form Work	4.55%	1,572.34	m2		7					1			100%	1,572.34		
Column Concrete & Curing & Form work removing	13.64%	472.43	m3			4	2	1					100%	472.43		
Beam Reinforcement & Insert plate installation	3.41%	29,671.61	kg	12						1			100%	29,671.61		
Beam Form Work	3.41%	494.11	m2		8					1			100%	494.11		
Beam Concrete & Curing & Form work removing	10.23%	81.81	m3			4	2	1					100%	81.81		
ST-30-006	19.43%	426.73											48%			61.49%
Foundation Coating	2.27%	155.14	m2			2							100%	155.14		
Foundation Back fill	4.55%	998.16	kg			4					1	2	100%	998.16		
Column Reinforcement & Insert plate & Anchore bolt installation	5.68%	25,943.78	kg	7						1			100%	25,943.78	21,205.02	81.73%
Column Form Work	4.55%	441.60	m2		4					1			100%	441.60	39.00	8.83%
Column Concrete & Curing & Form work removing	13.64%	88.32	m3			4	2	1					100%	88.32	27.00	30.57%
Beam Reinforcement & Insert plate installation	3.41%	8,191.42	kg	7						1			100%	8,191.42		
Beam Form Work	3.41%	690.32	m2		4					1			100%	690.32		
Beam Concrete & Curing & Form work removing	10.23%	125.13	m3			4	2	1					100%	125.13		
ST-50-006	1.46%	32.02											100%			
Excavation & Leveling & Compaction	7.00%	206.02	m3			2				1	1	2	100%	206.02		
Lean Concrete	1.50%	4.16	m3			2	2	1					100%	4.16		
Rebar Supply	5.00%	3,112.10	kg										100%	3,112.10		

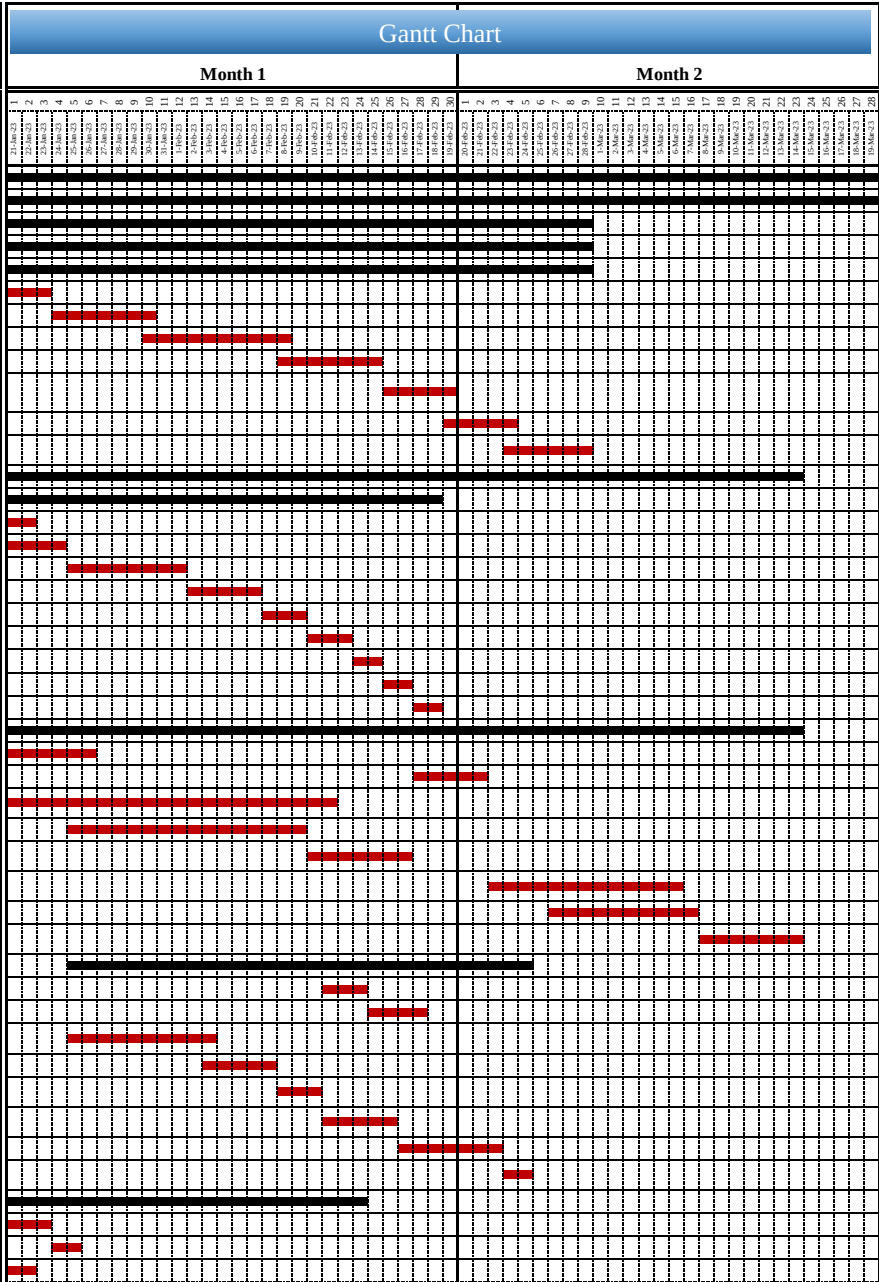

Sample Action Plan in Excel With Gantt Chart

Work Breakdown Structure (WBS)	WF %	Total Estimate	UM	Manpower			Equipment					Plan %	Plan QTY	Actual	Progress %	Start Date	Finish Date	Duration	
				Bar Bender	Form Worker	Worker	Truck Mixer	Concrete Pump	Crate	Excavator	Bobcat								Truck
Civil Sample Project	100.00%												37%			23.57%	01/11/1401	24/01/1402	83
Foundation Reinforcement	32.00%	3,112.10	kg	4					1	1			100%	3,112.10			03/11/1401	06/11/1401	4
Foundation Form Work	16.00%	24.00	m2		2					1			100%	24.00			07/11/1401	09/11/1401	3
Foundation Concrete & Curing & Form work removing	2.00%	22.50	m3			2	2	1					100%	22.50			10/11/1401	11/11/1401	2
Foundation Coating	18.00%	24.00	m2			2							100%	24.00			12/11/1401	13/11/1401	2
Foundation Back fill	1.00%	179.36	kg			2					1	1	100%	179.36			14/11/1401	15/11/1401	2
Column Reinforcement & Anchore bolt insatillation	1.50%	2,986.84	kg	4					1				100%	2,986.84			16/11/1401	19/11/1401	4
Column Form Work	6.00%	41.44	m2		2				1				100%	41.44			20/11/1401	22/11/1401	3
Column Concrete & Curing & Form work removing	10.00%	9.52	m3			2	2	1					100%	9.52			23/11/1401	24/11/1401	2
Reformer	2.15%	47.25											100%				01/11/1401	01/12/1401	31
Rebar Supply	7.41%	2,621.00	kg										100%	2,621.00			01/11/1401	02/11/1401	2
Foundation Reinforcement	22.22%	2,621.00	kg	3					1				100%	2,621.00			03/11/1401	06/11/1401	4
Foundation Form Work	11.85%	62.90	m2		3				1				100%	62.90			07/11/1401	09/11/1401	3
Foundation Concrete & Curing & Form work removing	26.67%	47.25	m3			2	3	1					100%	47.25			10/11/1401	11/11/1401	2
Foundation Back fill	5.93%	45.75	m3			2					1	3	100%	45.75			12/11/1401	19/11/1401	8
Column Reinforcement	2.22%	1,324.20	kg	2									100%	1,324.20			20/11/1401	25/11/1401	6
Column Form Work	5.93%	28.80	m2		2				1				100%	28.80			26/11/1401	29/11/1401	4
Column Concrete & Curing & Form work removing	17.78%	10.20	m3			2	3	1					100%	10.20			30/11/1401	01/12/1401	2
Administration Building	13.58%	1,320.20											51%		3.99%		01/11/1401	29/12/1401	59
Concrete Works	100.00%	1,320.20											51%		3.99%		01/11/1401	29/12/1401	59
Foundation	100.00%	1,320.20											51%		3.99%		01/11/1401	29/12/1401	59
Excavation	6.00%	3,422.66	m3						1	1	2		100%	3,422.66	2,273.60	66.43%	01/11/1401	16/11/1401	16
Grading & Compaction	1.00%	1,833.37	m2			4					1		100%	1,833.37			17/11/1401	22/11/1401	6
Lean Concrete	1.50%	163.63	m3			4	3	1					100%	163.63			23/11/1401	25/11/1401	3
Rebar Supply	10.00%	161,894.79	kg										100%	161,894.79			17/11/1401	19/11/1401	3
Reinforcement	32.00%	161,894.79	kg	12					1				100%	161,894.79			26/11/1401	29/12/1401	34
Ware house Building	1.77%												40%		71.78%		01/11/1401	19/11/1401	19
Steel Structure	100.00%	240,000.00											40%		71.78%		01/11/1401	19/11/1401	19
Installation	20.00%	240,000.00	kg			4			1				100%	162,079.10	144,325.30	89.05%	01/11/1401	12/11/1401	12
Alignment	8.00%	240,000.00	kg			4							100%	162,079.10			13/11/1401	14/11/1401	2
Bolting	8.00%	240,000.00	kg			4							100%	162,079.10			15/11/1401	16/11/1401	2
Touchup	3.00%	100.00	%			4							100%	100.00			17/11/1401	18/11/1401	2
Final Certificate	1.00%	100.00	%										100%	100.00			19/11/1401	19/11/1401	1
Road & Paving	21.02%	1,962.92											64%		6.50%		01/11/1401	24/01/1402	83
Dyke Wall	100.00%	1,962.92											64%		6.50%		01/11/1401	24/01/1402	83
Excavation	6.00%	3,208.90	m3							1	1	2	100%	3,208.90	320.89	10.00%	01/11/1401	08/11/1401	8
Grading & Compaction	1.00%	2,005.56	m2			4							100%	2,005.56	200.56	10.00%	09/11/1401	11/11/1401	3
Lean Concrete	1.50%	153.07	m3			4	3	1					100%	153.07	15.31	10.00%	12/11/1401	15/11/1401	4
Rebar Supply	5.00%	74,871.53	kg										100%	74,871.53	7,487.15	10.00%	05/11/1401	08/11/1401	4
Reinforcement FDN	15.00%	74,871.53	kg	8					1				100%	74,871.53	7,487.15	10.00%	16/11/1401	05/12/1401	20
Form Working FDN	8.00%	409.92	m3		5				1				100%	409.92	40.99	10.00%	06/12/1401	20/12/1401	15
Concrete Pouring FDN & Curing & Form work removing	12.00%	895.74	m3			4	3	1					100%	895.74	89.57	10.00%	21/12/1401	25/12/1401	5
Reinforcement Wall & Insert plate installation	15.00%	129,026.44	kg	8					1				100%	129,026.44	14,222.64	11.02%	26/12/1401	24/01/1402	28

